

Project	Enning Route B & C FTTH Upgrade 2023			
Contract No.	T23001			
Contract Date	1/5/2023			
Original Contract Price	\$ 3,330,205.98			
	Contract Price as Amended	Construction Miles	Construction Days	Service Entrances
Contract With Approved Amendments	\$ 4,699,254.46	198.79	120	148
Construction Released w/CAFs	\$ 4,699,254.46	198.79	120	148
Released Construction Miles	198.79	Construction Start Date:	Orig. Compl. Date:	Rev. Compl. Date:
Released Subscriber Entrances	148	5/2/2023	9/20/2023	11/7/2023
Released HBFO Splice Cases	223			
Total Frame Count Fibers	336			
Calculation of Construction Days		Days Startup		
	120	Days Rural Construction		
		Days Town Construction		
		Days Cleanup		
	120	Total Construction Days		
	1.66	Average Miles Required per Day		
Projected Route Miles to Date	137.50	miles		
Route Miles Constructed	133.49	miles		
Average Miles Constructed Per Day	1.61	miles		
Percent of Released Miles Completed	67.15%			
Inventory Complete Route Miles	98.03	miles		
Cleanup Complete Route Miles	98.03	miles		
Construction Days used	83	days		
Construction Delay - Rain	13	days		
Holidays or Non-Working Days	42	days		
Construction Days Remaining	37	days		
Percent of Construction Days Used	69.17%			
Service SEBV Installed	60	quantity		
Percent of Service SEBV Installed	40.54%			
Services Drops Installed	60	quantity		
Percent of Released Drops Completed	40.54%			
Percent Fiber Splicing Complete	47.15%			
Percent Fiber Splicing Tested	6.91%			
Percent Miles Inventoried	49.31%			
Delay Causes				
Remarks	See remarks Exhibit A			
Report By:	Heberly			
Report Date:	9/16/2023			

Remarks Exhibit A

Week Ending 9-16-2023 Enning Route B & C FTTH Upgrade 2023:

Equipment on-site:

- L&P Underground:
 - (1) Vermeer 24x40 directional drill

- MasTec:
 - (1) Dresser TD20 cable plow with Dresser TD20 lead dozer, (2) Case 580S backhoes and (1) CAT 420 backhoe
 - John Deere 450J clean-up dozer
 - Vermeer T655 rock saw
 - John Deere 333G skid steer with Harley-rake attachment
 - Vermeer 1250 cable plow

Construction work completed:

- Fourteen (14) BHF(24x36x30)T handholes set
- Two (2) BHF(30x48x36)T handholes set
- 2.87 mi (15166 ft) of BFO 12
- 8.45 mi (44630 ft) of BFO 24
- 3.20 mi (16920 ft) of BFO 48

Incidents:

- No incidents to report.


Project:

- No project updates for splicing.

Weekly totals:

- **Total BFO was 14.53 mi (76716 feet).**
- **Total SEBV for the week was 0.0 mi (0 feet).**
- **SEBV was installed to zero (0) subscriber locations.**
- **Drops were pulled to zero (0) subscriber locations**

Enning Route B

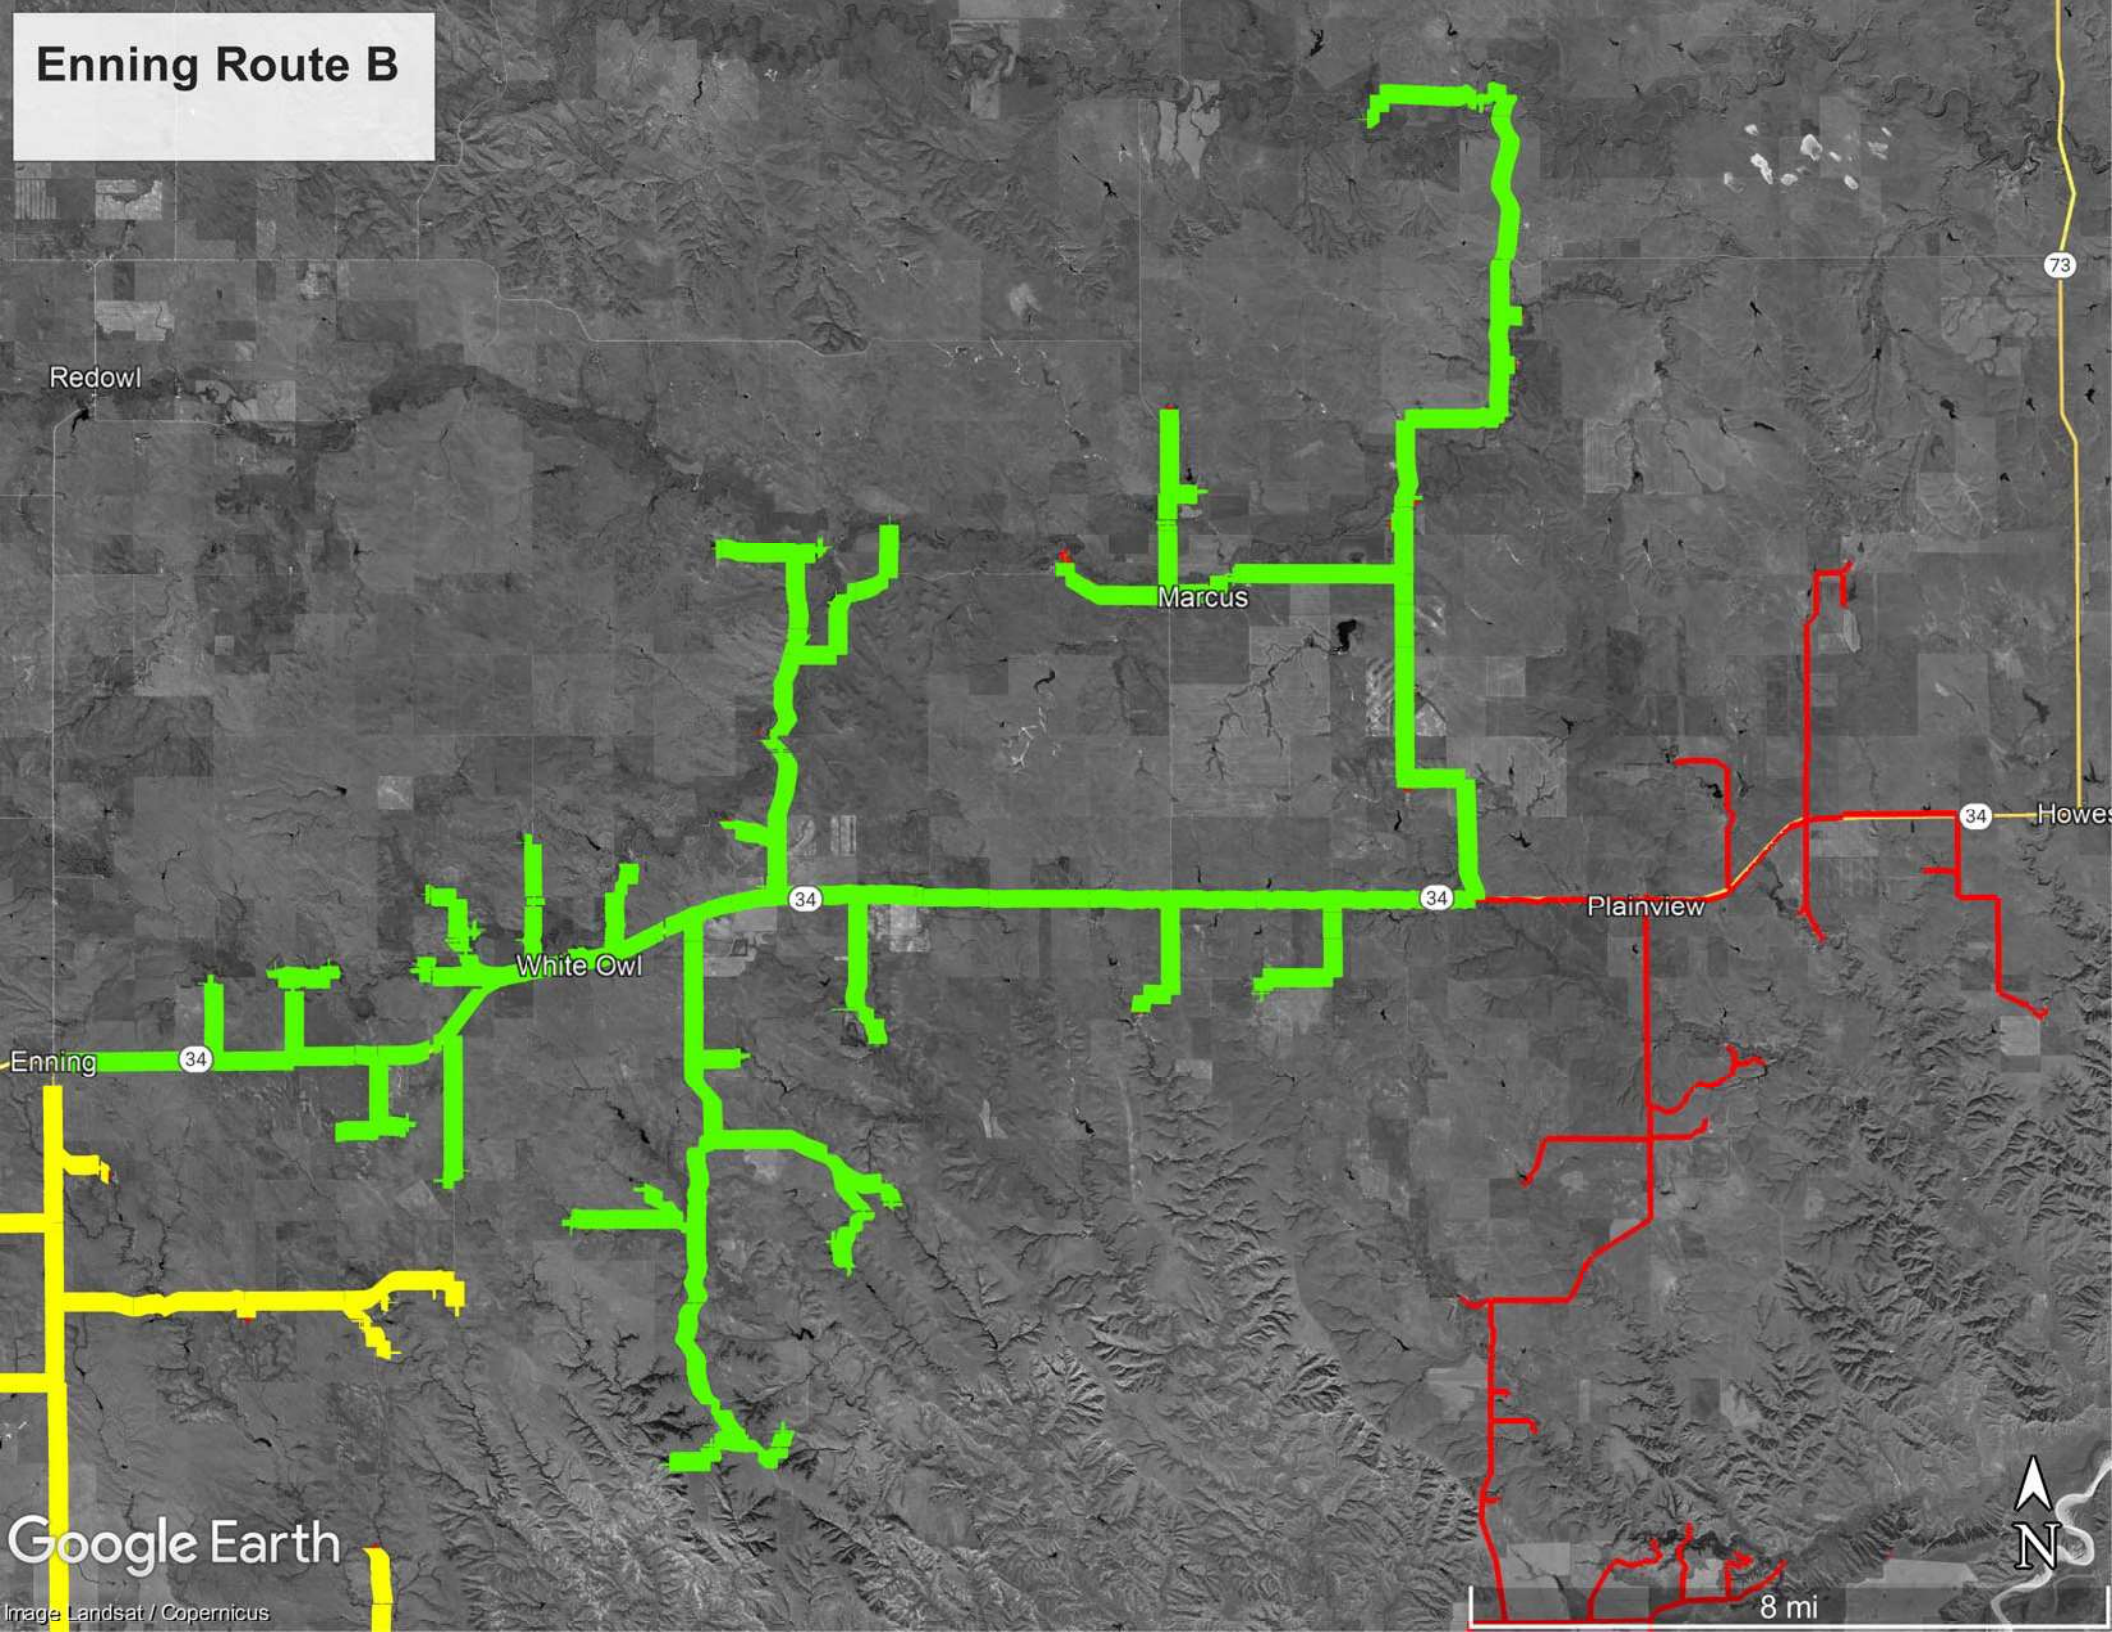

Redowl

Marcus

White Owl

Enning

Plainview

Howes



Project	Maurine FTTH Upgrade 2023			
Contract No.	T24001			
Contract Date	01/05/23			
Original Contract Price	\$ 2,824,532.85			
	Contract Price as Amended	Construction Miles	Construction Days	Service Entrances
Contract With Approved Amendments	\$ 3,800,686.03	185.68	120	97
Construction Released w/CAFs	\$ 3,800,686.03	185.68	120	97
Released Construction Miles	185.68	Construction Start Date:	Orig. Compl. Date:	Rev. Compl. Date:
Released Subscriber Entrances	97	5/2/2023	9/20/2023	10/26/2023
Released HBFO Splice Cases	157			
Total Frame Count Fibers	393			
Calculation of Construction Days		Days Startup		
	120	Days Rural Construction		
		Days Town Construction		
		Days Cleanup		
	120	Total Construction Days		
	1.55	Average Miles Required per Day		
Projected Route Miles to Date	140.81	miles		
Route Miles Constructed	177.45	miles		
Average Miles Constructed Per Day	1.95	miles		
Percent of Released Miles Completed	95.57%			
Inventory Complete Route Miles	58.24	miles		
Cleanup Complete Route Miles	58.24	miles		
Construction Days used	91	days		
Construction Delay - Rain	5	days		
Holidays or Non-Working Days	41	days		
Construction Days Remaining	29	days		
Percent of Construction Days Used	75.83%			
Service SEBV Installed	75	quantity		
Percent of Service SEBV Installed	77.32%			
Services Drops Installed	75	quantity		
Percent of Released Drops Completed	77.32%			
Percent Fiber Splicing Complete	50.00%			
Percent Fiber Splicing Tested	0.00%			
Percent Miles Inventoried	31.37%			
Delay Causes				
Remarks	See remarks Exhibit A			
Report By:	Heberly			
Report Date:	9/16/2023			

Remarks Exhibit A

Week Ending 9-16-2023 Maurine FTTH Upgrade 2023:

Equipment on-site:

- L&P Underground:
 - (1) Vermeer 24x40 directional drill

- MasTec:
 - (1) Cat D7R LGP cable plow with John Deere 950 lead dozer, (1) Case 580S backhoe and (1) CAT 420XE backhoe
 - John Deere 650J clean-up dozer with rake
 - (1) Vermeer 24x40 directional drill
 - (1) Vermeer 10x15 directional drill

Construction work completed:

- Three (3) BHF(24x36x30)T handholes set
- Two (2) BHF(30x48x36)T handholes set
- 1.55 mi (8214 ft) of BFO 12
- 2.87 mi (15204 ft) of BFO 48

Incidents:

- No incidents to report.

Project:

- B route (Deep Creek Rd) is ready for splicing.
 - 10 splice cases for this area
- C2A routes east of Opal school are ready for splicing.
 - 15 splice cases for this area
- C2A5 and C2A6 routes north and south of Opal school are ready for splicing.
 - 13 splice cases for this area
- D6 (Stomprud Rd), D9 (Cedar Canyon Rd), and D12C1 (Eagle Township Rd) are ready.
 - 13 splice cases for these areas
- D routes west of Mud Butte are ready for splicing.
 - 18 splice cases for this area

Weekly totals:

- **Total BFO was 4.43 mi (23418 feet).**
- **Total SEBV for the week was 0.18 mi (988 feet).**
- **SEBV was installed to six (6) subscriber locations.**
- **Drops were pulled to nine (9) subscriber locations.**

Maurine All Routes

